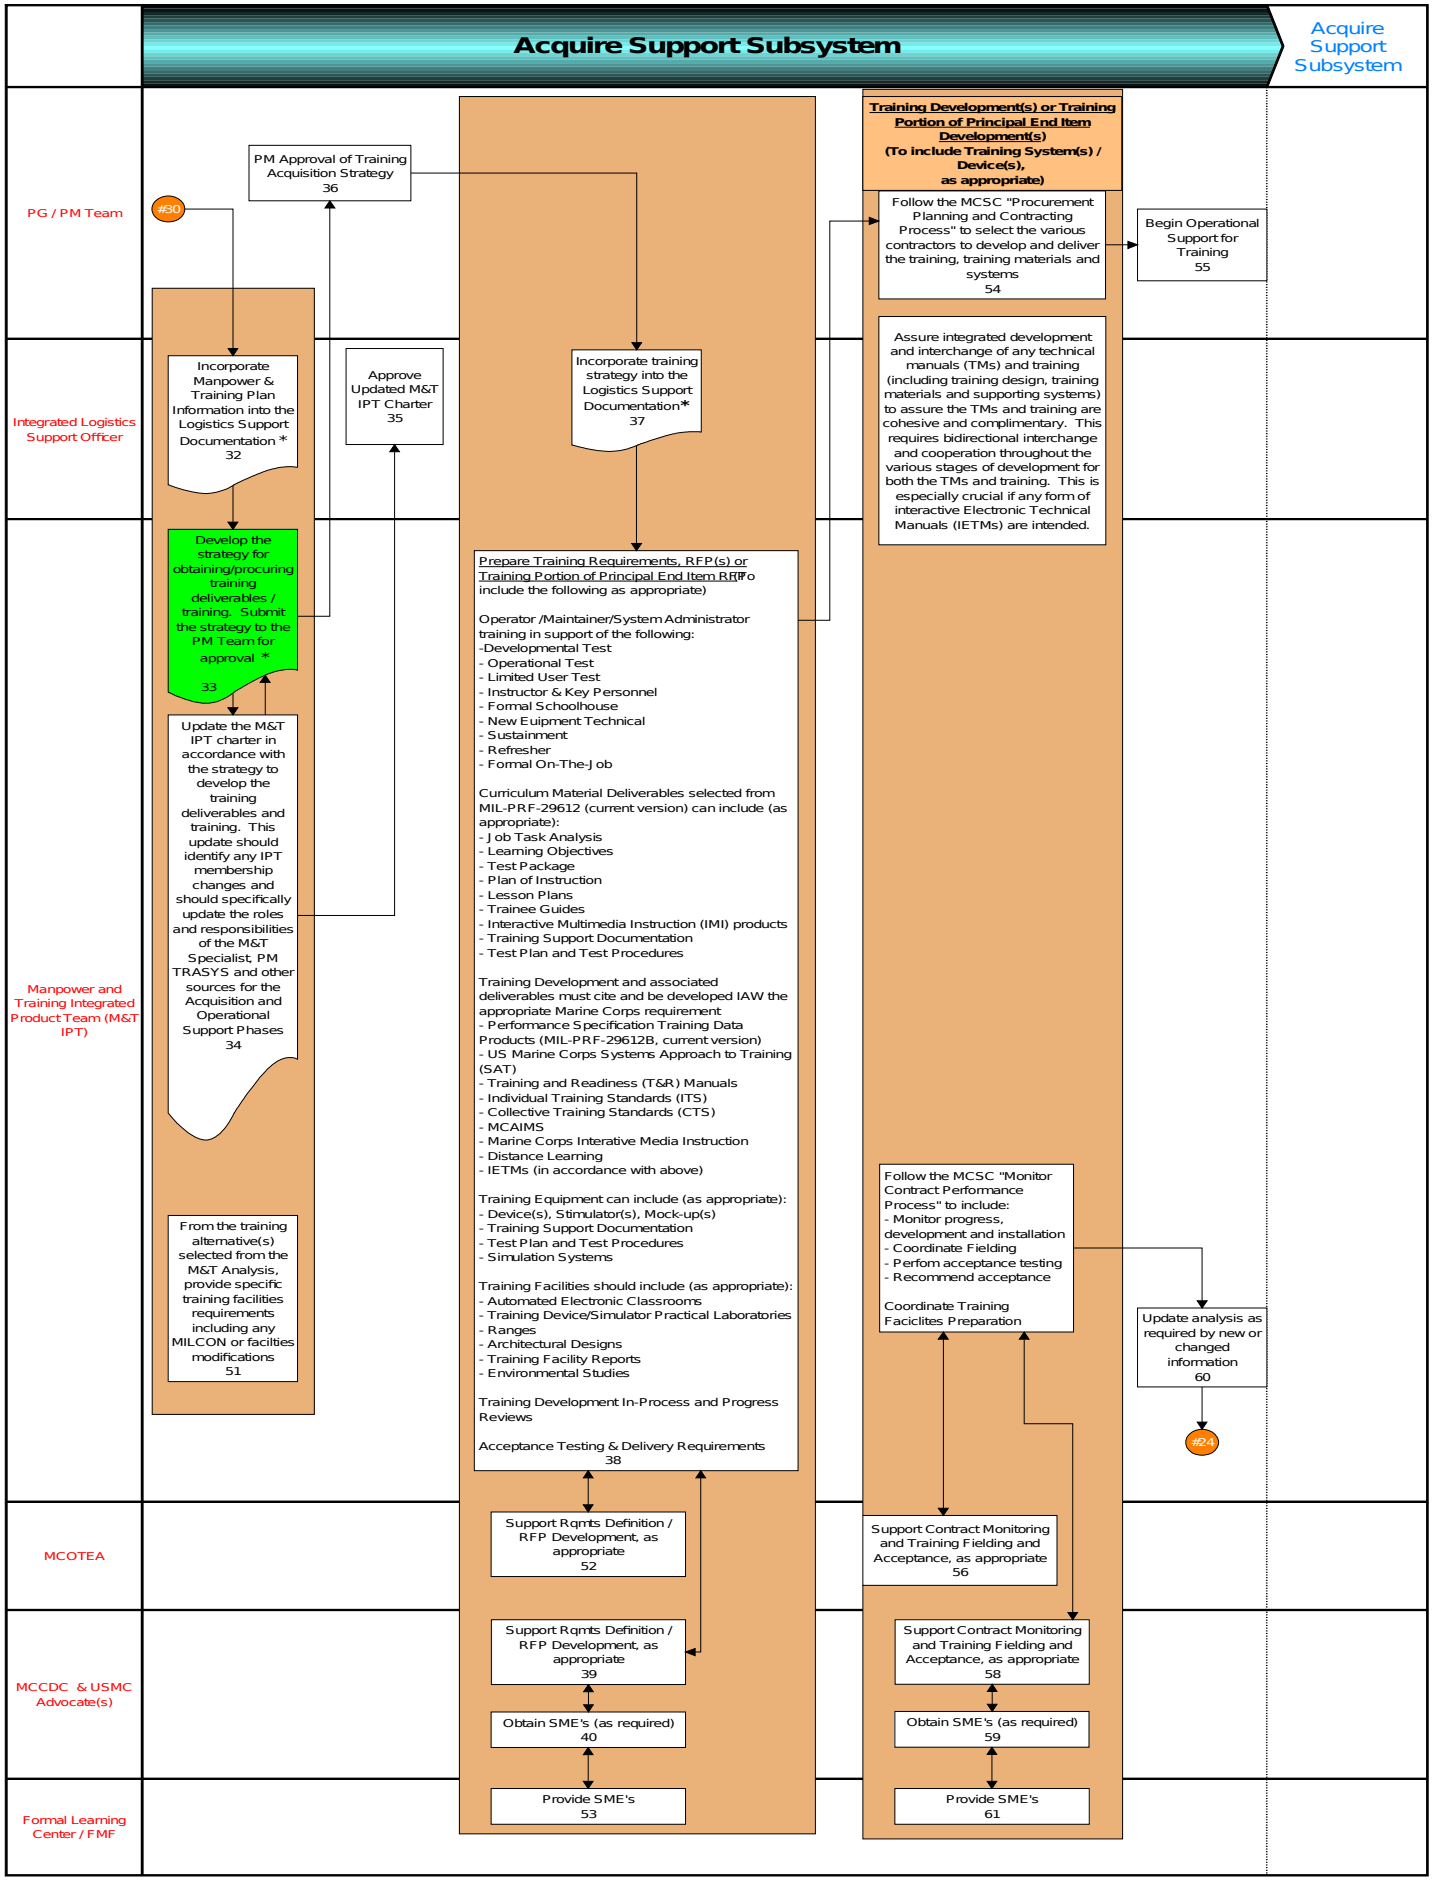
Acquire Support Subsystem
Acquire Support Subsystem
PG / PM Team
Integrated Logistics Support Officer
Manpower and Training Integrated Product Team (M&T IPT)
MCOTEA
MCCDC & USMC Advocate(s)
Formal Learning Center / FMF
#30
PM Approval of Training Acquisition Strategy 36
Incorporate Manpower & Training Plan Information into the Logistics Support Documentation * 32
Approve Updated M&T IPT Charter 35
Develop the strategy for obtaining/procuring training deliverables / training. Submit the strategy to the PM Team for approval * 33
Update the M&T IPT charter in accordance with the strategy to develop the training deliverables and training. This update should identify any IPT membership changes and should specifically update the roles and responsibilities of the M&T Specialist, PM TRASYS and other sources for the Acquisition and Operational Support Phases 34
From the training alternative(s) selected from the M&T Analysis, provide specific training facilities requirements including any MILCON or facilties modifications 51
Incorporate training strategy into the Logistics Support Documentation* 37
Prepare Training Requirements, RFP(s) or Training Portion of Principal End Item RFP to include the following as appropriate)
Operator /Maintainer/System Administrator training in support of the following:
-Developmental Test
- Operational Test
- Limited User Test
- Instructor & Key Personnel
- Formal Schoolhouse
- New Euipment Technical
- Sustainment
- Refresher
- Formal On-The-Job
Curriculum Material Deliverables selected from MIL-PRF-29612 (current version) can include (as appropriate):
- Job Task Analysis
- Learning Objectives
- Test Package
- Plan of Instruction
- Lesson Plans
- Trainee Guides
- Interactive Multimedia Instruction (IMI) products
- Training Support Documentation
- Test Plan and Test Procedures
Training Development and associated deliverables must cite and be developed IAW the appropriate Marine Corps requirement
- Performance Specification Training Data Products (MIL-PRF-29612B, current version)
- US Marine Corps Systems Approach to Training (SAT)
- Training and Readiness (T&R) Manuals
- Individual Training Standards (ITS)
- Collective Training Standards (CTS)
- MCAIMS
- Marine Corps Interative Media Instruction
- Distance Learning
- IETMs (in accordance with above)
Training Equipment can include (as appropriate):
- Device(s), Stimulator(s), Mock-up(s)
- Training Support Documentation
- Test Plan and Test Procedures
- Simulation Systems
Training Facilities should include (as appropriate):
- Automated Electronic Classrooms
- Training Device/Simulator Practical Laboratories
- Ranges
- Architectural Designs
- Training Facility Reports
- Environmental Studies
Training Development In-Process and Progress Reviews
Acceptance Testing & Delivery Requirements
38
Support Rqmts Definition / RFP Development, as appropriate 52
Support Rqmts Definition / RFP Development, as appropriate 39
Obtain SME's (as required) 40
Provide SME's 53
Training Development(s) or Training Portion of Principal End Item Development(s) (To include Training System(s) / Device(s), as appropriate)
Follow the MCSC "Procurement Planning and Contracting Process" to select the various contractors to develop and deliver the training, training materials and systems 54
Begin Operational Support for Training 55
Assure integrated development and interchange of any technical manuals (TMs) and training (including training design, training materials and supporting systems) to assure the TMs and training are cohesive and complimentary. This requires bidirectional interchange and cooperation throughout the various stages of development for both the TMs and training. This is especially crucial if any form of interactive Electronic Technical Manuals (IETMs) are intended.
Follow the MCSC "Monitor Contract Performance Process" to include:
- Monitor progress, development and installation
- Coordinate Fielding
- Perfom acceptance testing
- Recommend acceptance
Coordinate Training Faciclites Preparation
Update analysis as required by new or changed information 60
#24
Support Contract Monitoring and Training Fielding and Acceptance, as appropriate 56
Support Contract Monitoring and Training Fielding and Acceptance, as appropriate 58
Obtain SME's (as required) 59
Provide SME's 61

* Note: This documentation may stand alone, or may be incorporated within or appended to the Single Acquisition Management Plan (SAMP).
